


PURAVANKARA

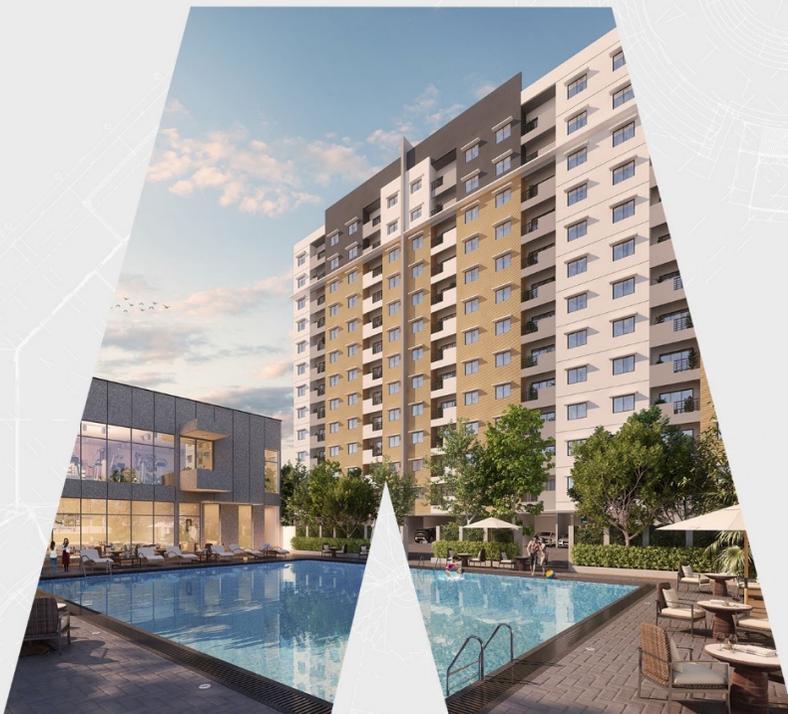

A
PURAVANKARA HOME AT
LAKEVISTA

Pride of owning something precious

LAKEVISTA
— AT —
PURVA
WINDERMERE
PALLIKARANAI

Construction Updates

Feb 2026

<https://www.puravankara.com/>


Dear Esteemed Customer,

Greetings from Puravankara

It gives us immense pleasure to update you through this edition of Puravankara Newsletter and provide you with the latest information about your home in Lakevista. As we move ahead, we at Puravankara sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

*We are grateful for your kind cooperation.
Team Lakevista*

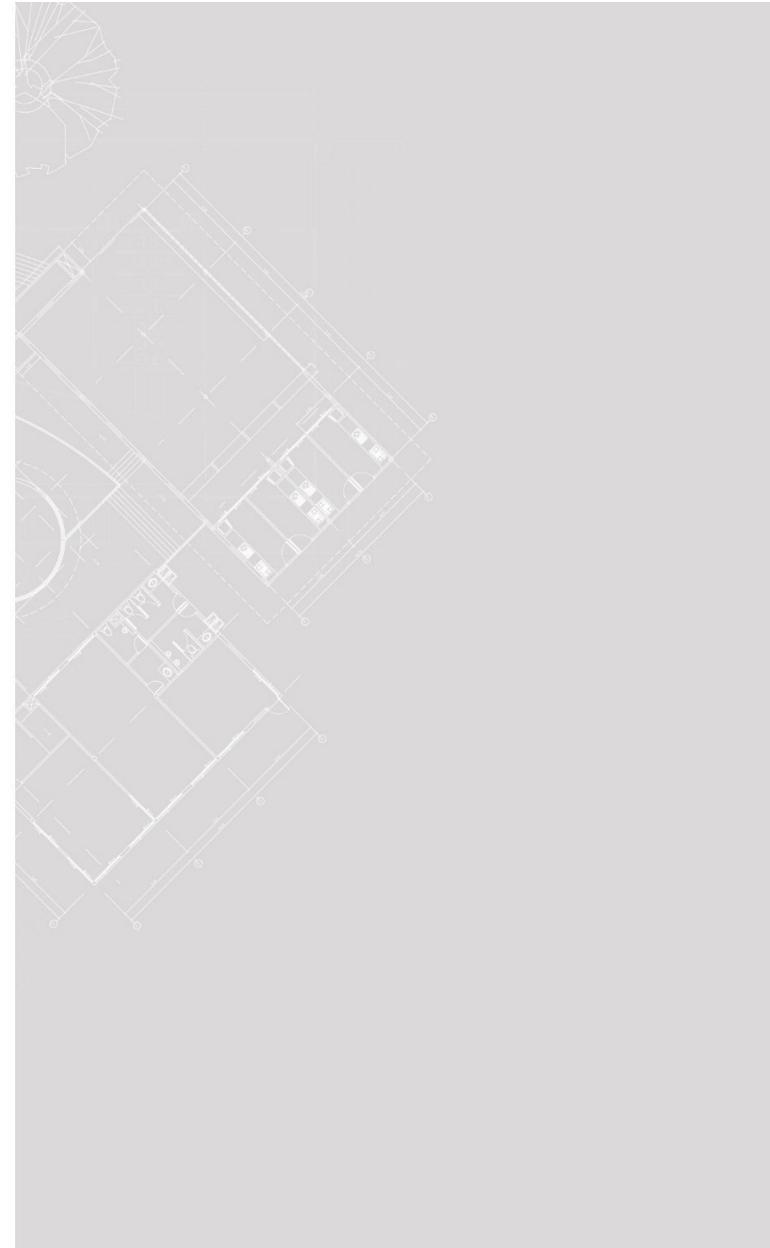



Lakevista

Pallikaranai, Chennai



Construction Updates

Overall view



Tower K

TOWER STATUS

- Structure Completed.
- Tiling Completed.
- 4th & 5th Floor Window Installation & 3rd Floor Door Installation in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Gypsum Plaster Completed.
- Tiling Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Doors & Windows till 7th Floor.
- Completion of Exterior Texture

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26



Tower M3

TOWER STATUS

- Tiling works completed.
- Joinery Completed.
- Exterior Texture and Painting in Progress.
- CP & Sanitary Installation in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling Completed.
- Joinery completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Exterior Texture and Paint.
- Completion of Internal Painting.
- CP & Sanitary Installation till 05th Floor.

PROGRESS TIMELINE





Tower M2

TOWER STATUS

- Terrace Floor Slab Completed.
- 8th Floor Internal Gypsum Plaster in Progress.
- 1st, 2nd & 3rd Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Terrace Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster till 10th Floor.
- Completion of Tiling till 4th Floor.

PROGRESS TIMELINE





Tower M1

TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- 10th & 11th Floor Tiling in Progress



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling till 9th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling.
- Completion of Doors & Windows till 3rd Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower P4

TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- 11th Floor Tiling works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling till 10th Floor Completed.
- Doors & Windows till 2nd Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion till 11th Floor Tiling.
- Completion of Doors & Windows till 5th Floor.
- Completion of Exterior Texture.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower E15

TOWER STATUS

- Structure Completed.
- Internal Plaster Completed.
- 7th Floor Tiling in Progress.
- Exterior Texture in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Blockwork Completed.
- Internal & External Plaster Completed.
- Tiling till 06th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling.
- Completion of Exterior Texture.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26



Tower P3

TOWER STATUS

- Tower P3 Pour 01 Terrace Slab Completed & Pour 02 11th Floor Slab in progress.
- 5th Floor Internal Gypsum Plaster in Progress.
- 1st Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- P3 Pour 01 Terrace Floor Slab & Pour 02 10th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Terrace Floor Slab in Pour 2.
- Completion of Internal Gypsum Plaster till 7th Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower L

TOWER STATUS

- Tower LA, LC Terrace Slab Completed.
- LB pour 01 Terrace Floor Slab in Progress.
- Tower LB pour 02 12th Floor Slab in Progress.
- 4th Floor Internal Gypsum Plaster in Progress.
- 1st & 2nd Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Tower LA & LC Terrace Floor Slab, LB pour 01 12th Floor Slab & Tower LB pour 02 11th Floor Slab Completed.
- Internal Gypsum Plaster till 3rd Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of LB Terrace Floor Slab.
- Completion of Internal Gypsum Plaster till 5th Floor.
- Completion of Tiling till 2nd Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower P2

TOWER STATUS

- Tower P2 Pour 01 Terrace Completed and Pour 2 12th Floor Slab works in progress.
- 3rd & 4th Floor Internal Gypsum Plaster in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Pour 01 Terrace Floor Slab & Pour 02 11th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Terrace Floor slab – Pour 02.
- Completion of Gypsum Plaster till 06th Floor.

PROGRESS TIMELINE





Tower M4

TOWER STATUS

- 4th Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 3rd Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 5th Floor Slab.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower M5

TOWER STATUS

- 8th Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 7th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 9th Floor Slab.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower P1

TOWER STATUS

- Stilt Floor Completed.
- Pour 01 4th Floor Slab in progress.
- Pour 02 2nd Floor Slab in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.
- Pour 01 3rd Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 3rd & 5th Floor Slab.

PROGRESS TIMELINE





Tower M7

TOWER STATUS

- Tower M7 Plinth works completed.
- Stilt Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Stilt Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



Tower M6

TOWER STATUS

- Tower M6 Foundation works in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Foundation.
- Completion of Plinth works.

PROGRESS TIMELINE



February 26


MLCP 1



TOWER STATUS

- Pour 01 Terrace Slab in Progress.
- Pour 02 1st Floor Slab in Progress.
- Pour 03 Excavation in Progress.

Internal Finishes - Tiling

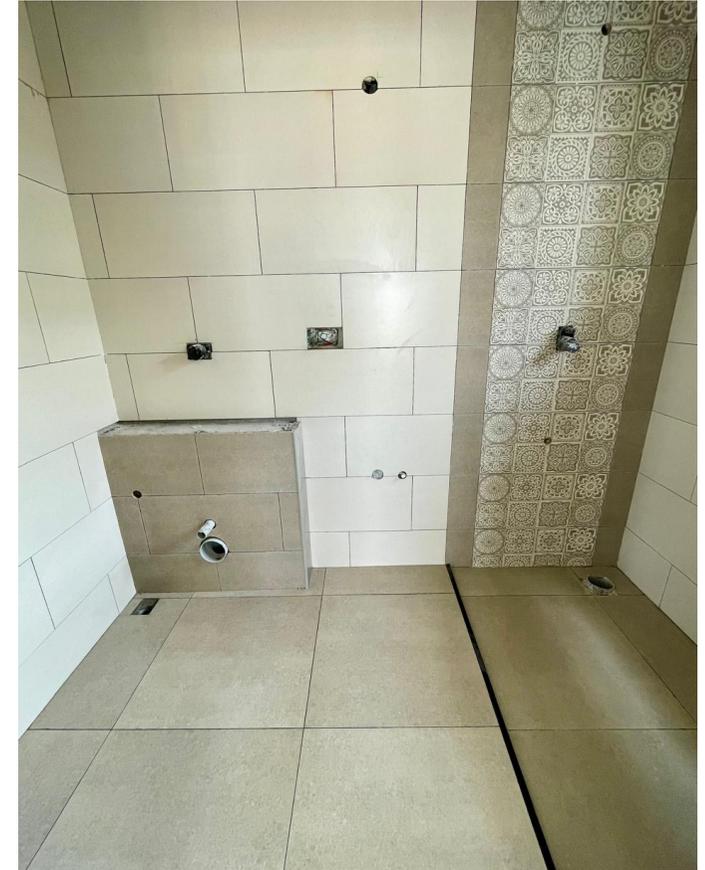

TOWER STATUS

- Tower K Completed.
- Tower M3 Completed.
- Tower M1 10th & 11th Floor in Progress.
- Tower P4 11th Floor in Progress.
- Tower E15 7th Floor in Progress.
- Tower L 1st & 2nd Floor in Progress.
- Tower P3 1st Floor in Progress.

Internal Finishes - Joinery



TOWER STATUS - WINDOWS

- Tower K 4th & 5th Floor in Progress.
- Tower M3 Completed.
- Tower P4 6th Floor in Progress.

TOWER STATUS - DOORS

- Tower K 3rd Floor in Progress.
- Tower M3 Completed.
- Tower P4 3rd Floor in Progress.

Contact us

Site Office :

No: 14 Surya Nagar, Erikarai Road,
Pallikaranai, Chennai - 600100.

Regional Office :

Puravankara Limited. #130/1, Ulsoor Road,
Bengaluru - 560 042

Email : crm@puravankara.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.puravankara.com

RERA Registration Number :

RERA No: TN/29/BUILDING/0008/2023 | TN/29/BUILDING/0009/2023 |
TN/29/BUILDING/0010/2023
