PURAVANKARA



PURAVANKARA HOME AT LAKEVISTA

Pride of owning something precious



Construction Updates
October 2025

Dear Esteemed Customer,

Greetings from Puravankara

It gives us immense pleasure to update you through this edition of Puravankara Newsletter and provide you with the latest information about your home in Lakevista. As we move ahead, we at Puravankara sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation. Team Lakevista





Lakevista

Pallikaranai, Chennai



Construction Updates

Overall view

Tower K



Actual site photograph

PROGRESS TIMELINE



TOWER STATUS

- Terrace Slab Completed.
- 12th Floor Internal Gypsum Plaster in Progress.
- 6th,7th & 8th Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Terrace Slab Completed.
- Gypsum Plaster Completed till 11th Floor.
- Tiling Completed till 05th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Gypsum Plaster Completion.
- Tiling Completion till 07th Floor.



TOWER STATUS

- Terrace floor slab completed.
- Tiling works completed.
- 6th & 11th Floor Joinery in Progress.
- Exterior Texture and Painting in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Tower M3 terrace slab.
- · Tiling completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Joinery.
- Completion of Exterior Texture and Paint.

Actual site photograph





TOWER STATUS

- Terrace Floor Slab in progress.
- 3rd Floor Internal Gypsum Plaster in Progress.



CONSTRUCTION MILESTONES ACHIEVED

• 11th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Terrace Slab.
- Completion of Internal Gypsum Plaster till 05th Floor.

Actual site photograph





Actual site photograph

PROGRESS TIMELINE



TOWER STATUS

- Terrace Floor Slab Completed.
- 11th Floor Internal Gypsum Plaster in Progress.
- 04th, 05th & 06th Floor Tiling in Progress



CONSTRUCTION MILESTONES ACHIEVED

- Terrace Floor Slab Completed.
- Tiling till 03rd Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster.
- Completion of Tiling till 6th Floor.



TOWER STATUS

- Terrace Slab Completed
- 9th, 10th & 11th Floor Internal Gypsum Plaster in progress.
- 6th & 7th Floor Tiling works in progress.



CONSTRUCTION MILESTONES ACHIEVED

Terrace Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster.
- Completion till 8th Floor Tiling.

Actual site photograph



Tower E15



Actual site photograph

PROGRESS TIMELINE



TOWER STATUS

- Terrace Floor Slab Completed.
- 09th Floor Internal Plaster in Progress.
- 1st Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Terrace Floor Slab Completed.
- Blockwork completed.
- External Plaster Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of Internal Plaster.



Actual site photograph

TOWER STATUS

- Tower P3 Pour 01 10th Floor Slab & Pour 02 6th Floor Slab in progress.
- 1st Floor Internal Gypsum Plaster in Progress.



CONSTRUCTION MILESTONES ACHIEVED

 P3 Pour 01 9th Floor Slab & Pour 02 05th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of 11th & 7th Floor Slab.



Tower L



TOWER STATUS

- Tower LA, LC, LB pour 01 9th Floor Slab in Progress.
- Tower LB pour 02 5th Floor Slab in Progress.
- 1st Floor Internal Gypsum Plaster in Progress.



CONSTRUCTION MILESTONES ACHIEVED

 Tower LC, LB pour 01, Tower LA 7th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of 5th ,7th & 9th Floor slab.

Actual site photograph





TOWER STATUS

Tower P2 5th & 8th Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

• 3rd & 7th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of 5th & 9th Floor slab.

Actual site photograph





Actual site photograph

PROGRESS TIMELINE



TOWER STATUS

- Stilt Slab Completed.
- 2nd Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

• 1st Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of 3rd Floor Slab.



TOWER STATUS

• Stilt Slab in Progress.



CONSTRUCTION MILESTONES ACHIEVED

• Stilt Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of 3rd Floor Slab.

Actual site photograph





TOWER STATUS

• Tower P1 Plinth works & Stilt Floor Column in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of Plinth.

Actual site photograph





TOWER STATUS

• Tower M7 Columns till Plinth level in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.



UPCOMING CONSTRUCTION MILESTONES

• Completion of Plinth.

Actual site photograph




Internal Finishes - Tiling



TOWER STATUS

- Tower K 6th to 8th Floor in Progress.
- Tower M3 Completed.
- Tower M1 4th to 6th Floor in Progress.
- Tower P4 6th & 7th Floor in Progress.
- Tower E15 1st Floor in Progress.

Internal Finishes - Joinery

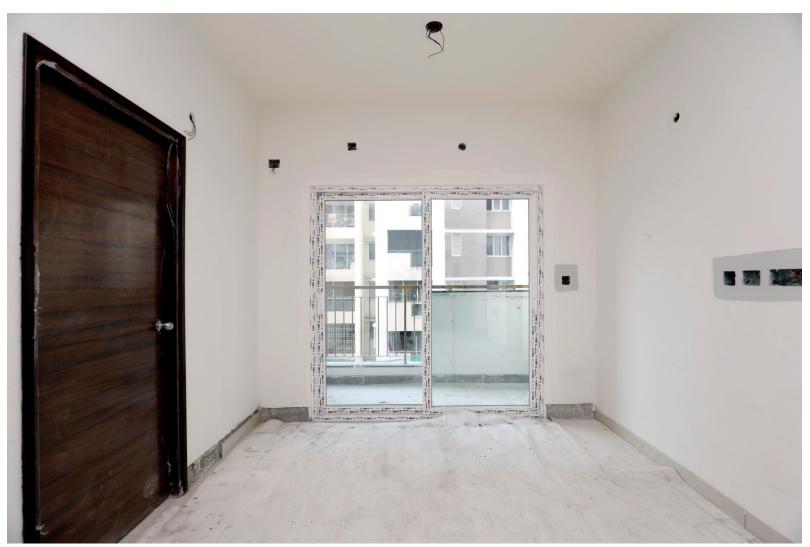

TOWER STATUS - WINDOWS

- Tower K 2nd & 3rd Floor in Progress.
- Tower M3 6th to 11th Floor in Progress.
- Tower P4 1st & 2nd Floor in Progress.

TOWER STATUS - DOORS

- Tower K 2nd Floor in Progress.
- Tower M3 2nd to 06th Floor in Progress.

Contact us

PURAVANKARA

Site Office:

No: 14 Surya Nagar, Erikarai Road, Pallikaranai, Chennai - 600100.

Regional Office:

Puravankara Limited. #130/1, Ulsoor Road, Bengaluru - 560 042

Email: crm@puravankara.com (Subject line - Project name/ unit number)

Call Us: +91 - 80-67724001 / 1 860 208 0000

Web: www.puravankara.com

RERA Registration Number:

RERA No: TN/29/BUILDING/0008/2023 | TN/29/BUILDING/0009/2023 | TN/29/BUILDING/0010/2023
