

PURAVANKARA



A
PURAVANKARA HOME AT
LAKEVISTA

Pride of owning something precious

LAKEVISTA
— AT —
PURVA
WINDERMERE
PALLIKARANAI

Construction Updates
April 2026

<https://www.puravankara.com/>


Dear Esteemed Customer,

Greetings from Puravankara

It gives us immense pleasure to update you through this edition of Puravankara Newsletter and provide you with the latest information about your home in Lakevista. As we move ahead, we at Puravankara sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

*We are grateful for your kind cooperation.
Team Lakevista*

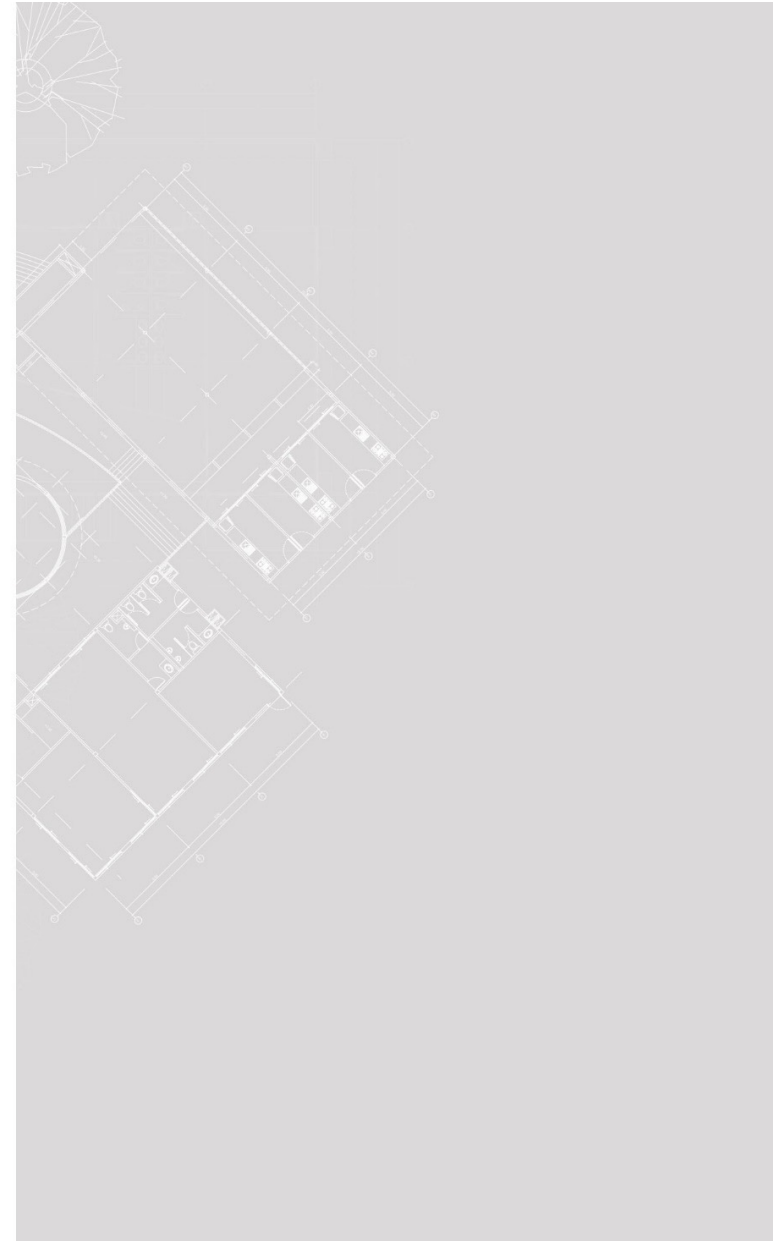



Lakevista

Pallikaranai, Chennai



Construction Updates

Overall view



Tower K

TOWER STATUS

- Structure Completed.
- Tiling Completed.
- 7th & 8th Floor Windows & Door Installation in Progress.
- 1st to 3rd Floor Internal Painting in Progress.
- External Texture and Painting works in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling Completed.
- Doors & Windows Completed till 6th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Doors & Windows till 8th Floor.
- Completion of Exterior Texture & Painting.
- Completion of Internal 1st coat painting till 4th Floor.

PROGRESS TIMELINE





Tower M3

TOWER STATUS

- Tiling works completed.
- Joinery Completed.
- Exterior Texture and Painting in Progress.
- Internal Painting 1st Coat completed.
- 6th Floor CP & Sanitary Installation in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling Completed.
- Joinery completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Exterior Texture and Painting.
- CP & Sanitary Installation till 08th Floor.
- Completion of Internal 2nd Coat painting till 3rd Floor.

PROGRESS TIMELINE





Tower M2

TOWER STATUS

- Terrace Floor Slab Completed.
- Internal Gypsum Plaster Completed.
- 5th & 6th Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Terrace Slab Completed.
- Tiling Completed till 4th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling till 7th Floor.
- Completion of Doors & Windows till 2nd Floor.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26



Tower M1

TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- 11th Floor Tiling in Progress.
- 5th to 7th Floor Doors & Windows in Progress.
- Exterior Texture and Painting in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling till 10th Floor Completed.
- Doors & Windows Completed till 4th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling.
- Completion of Doors & Windows till 6th Floor.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26



Tower P4

TOWER STATUS

- Structure Completed.
- Internal Gypsum Plaster Completed.
- Tiling Works Completed.
- Windows installation progress in 7th, 8th Floor & Doors in 5th, 6th Floor.
- Exterior Texture & Painting in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Tiling works Completed.
- Doors & Windows till 4th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Doors & Windows till 6th Floor.
- Completion of Exterior Texture & Painting.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26



Tower E15

TOWER STATUS

- Structure Completed.
- Internal Plaster Completed.
- 9th & 10th Floor Tiling in Progress.
- Exterior Texture & painting in Progress.
- Doors & Windows installation progress in 1st Floor.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal & External Plaster Completed.
- Tiling till 08th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Tiling.
- Completion of Exterior Texture & Painting.
- Completion of Doors & Windows till 2nd Floor.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26



Tower P3

TOWER STATUS

- Structure Completed.
- 9th Floor Internal Gypsum Plaster in Progress.
- 1st to 3rd Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal Gypsum Plaster Completed till 8th Floor.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster till 10th Floor.
- Completion of Tiling till 3rd Floor.

PROGRESS TIMELINE



Tower L



TOWER STATUS

- Structure Completed.
- 5th Floor Internal Gypsum Plaster in Progress.
- 1st, 2nd & 3rd Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal Gypsum Plaster till 4th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Internal Gypsum Plaster till 6th Floor.
- Completion of Tiling till 3rd Floor.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



Tower P2

TOWER STATUS

- Structure Completed
- 5th Floor Internal Gypsum Plaster in Progress.
- 1st Floor Tiling in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Structure Completed.
- Internal Gypsum Plaster till 4th Floor Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Gypsum Plaster till 06th Floor.
- Completion of 1st Floor Tiling.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26



Tower M4

TOWER STATUS

- 7th Floor Slab works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- 6th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 7th Floor Slab.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26



Tower M5

TOWER STATUS

- 12th Floor Slab works in progress.
- 1st Floor Internal Gypsum Plaster in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- 11th Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 12th Floor Slab.

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26

Construction Updates

Tower P1



TOWER STATUS

- Stilt Floor Completed.
- Pour 01 7th Floor Slab in progress.
- Pour 02 4th Floor Slab in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.
- Pour 01 6th Floor Slab & Pour 02 3rd Floor Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 5th & 7th Floor Slab.

PROGRESS TIMELINE



October 25

November 25

December 25

January 26

February 26

March 26

Construction Updates



Tower M7

TOWER STATUS

- Stilt Floor Slab works completed.
- 2nd Floor Slab works in Progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.
- Stilt Slab Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of 3rd Floor Slab..

PROGRESS TIMELINE



October 25



November 25



December 25



January 26



February 26



March 26

Construction Updates



Tower M6

TOWER STATUS

- Tower M6 Plinth & Stilt Floor works in progress.



CONSTRUCTION MILESTONES ACHIEVED

- Excavation Completed.
- Foundation Completed.



UPCOMING CONSTRUCTION MILESTONES

- Completion of Plinth & Stilt Floor works.

PROGRESS TIMELINE



February 26

March 26


MLCP 1



TOWER STATUS

- Pour 01 & Pour 02 Terrace Slab Completed.
- Pour 03 Excavation in Progress.

Internal Finishes - Tiling

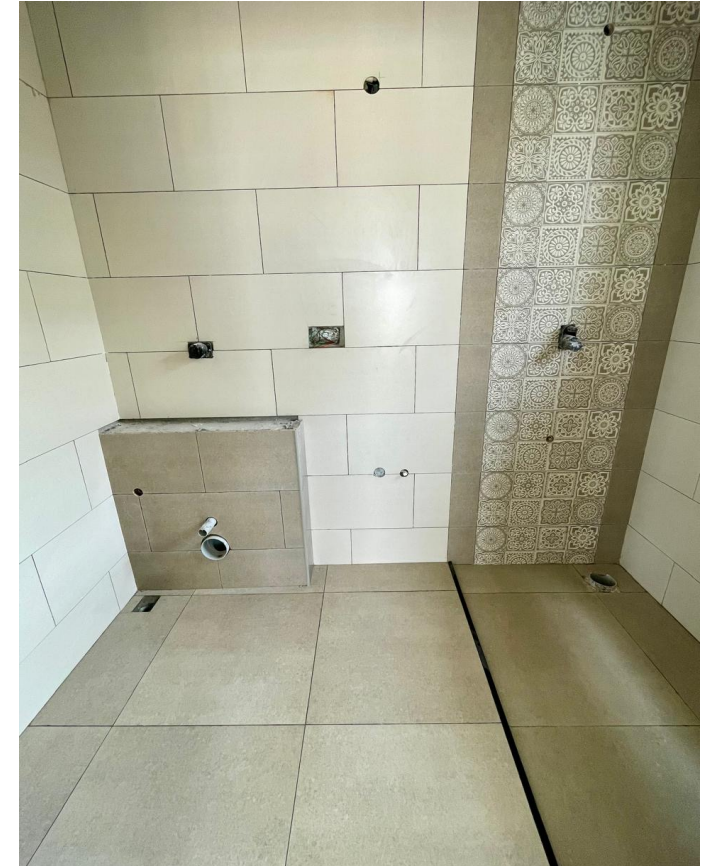

TOWER STATUS

- Tower K Completed.
- Tower M3 Completed.
- Tower M1 11th Floor in Progress.
- Tower P4 Completed.
- Tower E15 9th & 10th Floor in Progress.
- Tower L 1st, 2nd & 3rd Floor in Progress.
- Tower P3 1st, 2nd & 3rd Floor in Progress..

Construction Updates

Internal Finishes - Joinery



TOWER STATUS - WINDOWS

- Tower K 7th & 8th Floor in Progress.
- Tower M3 Completed.
- Tower P4 7th & 8th Floor in Progress.
- Tower M1 5th to 7th Floor in Progress.
- Tower E15 1st Floor in Progress.

TOWER STATUS - DOORS

- Tower K 6th Floor in Progress.
- Tower M3 Completed.
- Tower P4 5th & 6th Floor in Progress.
- Tower M1 5th to 7th Floor in Progress.
- Tower E15 1st Floor in Progress.

Contact us

Site Office :

No: 14 Surya Nagar, Erikarai Road,
Pallikaranai, Chennai - 600100.

Regional Office :

Puravankara Limited. #130/1, Ulsoor Road,
Bengaluru - 560 042

Email : crm@puravankara.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.puravankara.com

RERA Registration Number :

RERA No: TN/29/BUILDING/0008/2023 | TN/29/BUILDING/0009/2023 |
TN/29/BUILDING/0010/2023
